
WarpView build swimlane — 1 orchestrator · 18 agent slots · every ticket merges when green

16 tickets · 6 waves · 127 agent-hours · finish T+59h · peak 6 in flight · critical chain 56.5h over 6 tickets

★ WV-01 → WV-06 → WV-07 → WV-09 → WV-15 → WV-16

platform · model · console · quality · release · ★ critical chain · gate reached (gate blocks run in order)

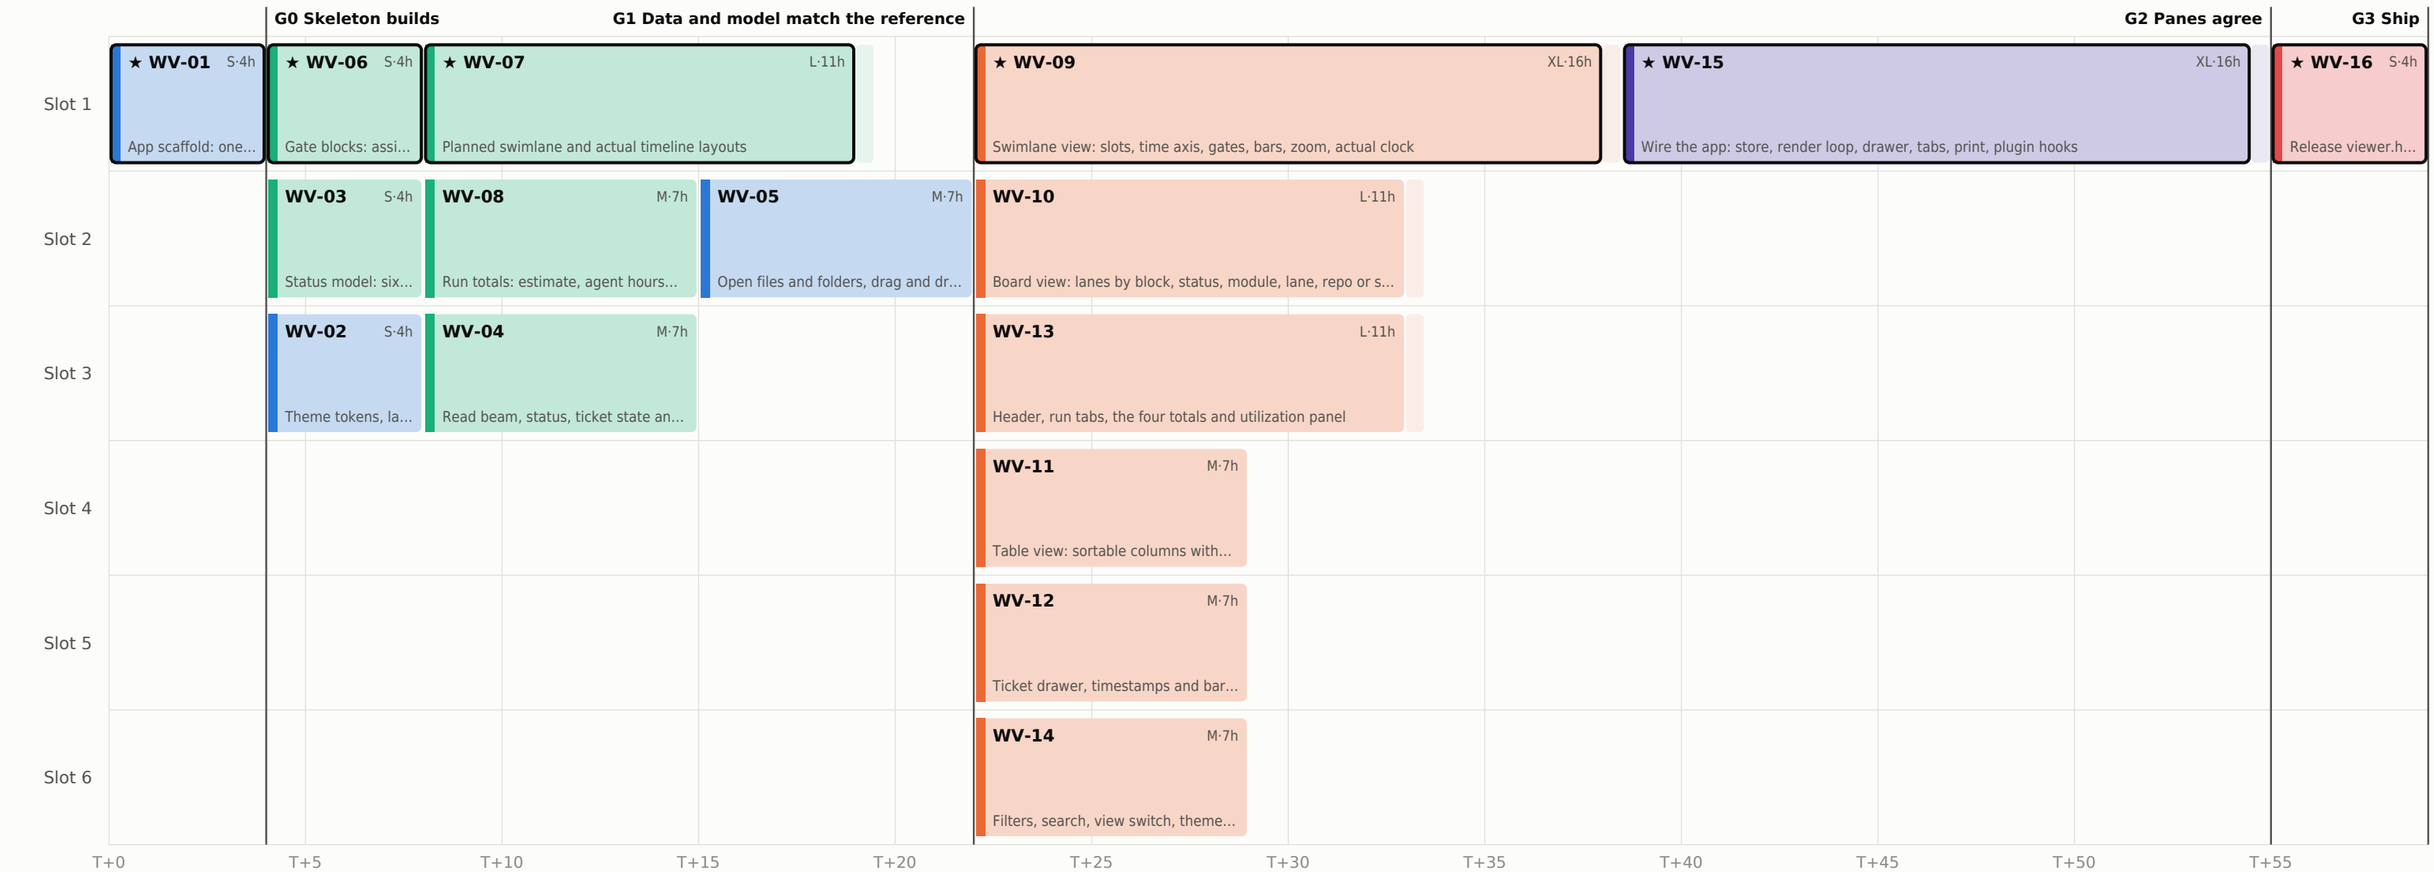

Estimate-hours on a continuous clock. Solid = the agent works; pale = an L/XL PR waits for approval before dependents start. A slot is reused the moment its agent finishes.

Step table — every merge moment

One row per moment something merges: what lands, the gate it reaches, what starts on which slot.

#	At	Merges	Gate	Starts (ticket → slot)	In flight
0	**T+0h**	start		★ WV-01 → 1	1
1	**T+4h**	★ WV-01	**G0 Skeleton builds**	★ WV-06 → 1, WV-03 → 2, WV-02 → 3	3
2	**T+8h**	WV-02, WV-03, ★ WV-06		★ WV-07 → 1, WV-08 → 2, WV-04 → 3	3
3	**T+15h**	WV-04, WV-08		WV-05 → 2	2
4	**T+19h**	start		—	2
5	**T+19.5h**	★ WV-07		—	1
6	**T+22h**	WV-05	**G1 Data and model match the reference**	★ WV-09 → 1, WV-10 → 2, WV-13 → 3, WV-11 → 4, WV-12 → 5, WV-14 → 6	6
7	**T+29h**	WV-11, WV-12, WV-14		—	3
8	**T+33h**	start		—	3
9	**T+33.5h**	WV-10, WV-13		—	1
10	**T+38h**	start		—	1
11	**T+38.5h**	★ WV-09		★ WV-15 → 1	1
12	**T+54.5h**	start		—	1
13	**T+55h**	★ WV-15	**G2 Panes agree**	★ WV-16 → 1	1
14	**T+59h**	★ WV-16	**G3 Ship**	—	0

T+ = estimate-hours. Starts are ticket → slot. Detail per start: BUILD_PLAN.md.

Slot sequences

Start → merge in estimate-hours, per slot.

Slot	Tickets	Busy	Sequence
Slot 1	6	55h	★ WV-01 (0–4) → ★ WV-06 (4–8) → ★ WV-07 (8–19.5) → ★ WV-09 (22–38.5) → ★ WV-15 (38.5–55) → ★ WV-16 (55–59)
Slot 2	4	29h	WV-03 (4–8) → WV-08 (8–15) → WV-05 (15–22) → WV-10 (22–33.5)
Slot 3	3	22h	WV-02 (4–8) → WV-04 (8–15) → WV-13 (22–33.5)
Slot 4	1	7h	WV-11 (22–29)
Slot 5	1	7h	WV-12 (22–29)
Slot 6	1	7h	WV-14 (22–29)
