
WarpEdit build swimlane — 1 orchestrator · 18 agent slots · every ticket merges when green

14 tickets · 7 waves · 110 agent-hours · finish T+76h · peak 3 in flight · critical chain 69h over 7 tickets

★ WE-01 → WE-02 → WE-04 → WE-05 → WE-11 → WE-12 → WE-14

platform · model · console · quality · release · ★ critical chain · gate reached (gate blocks run in order)

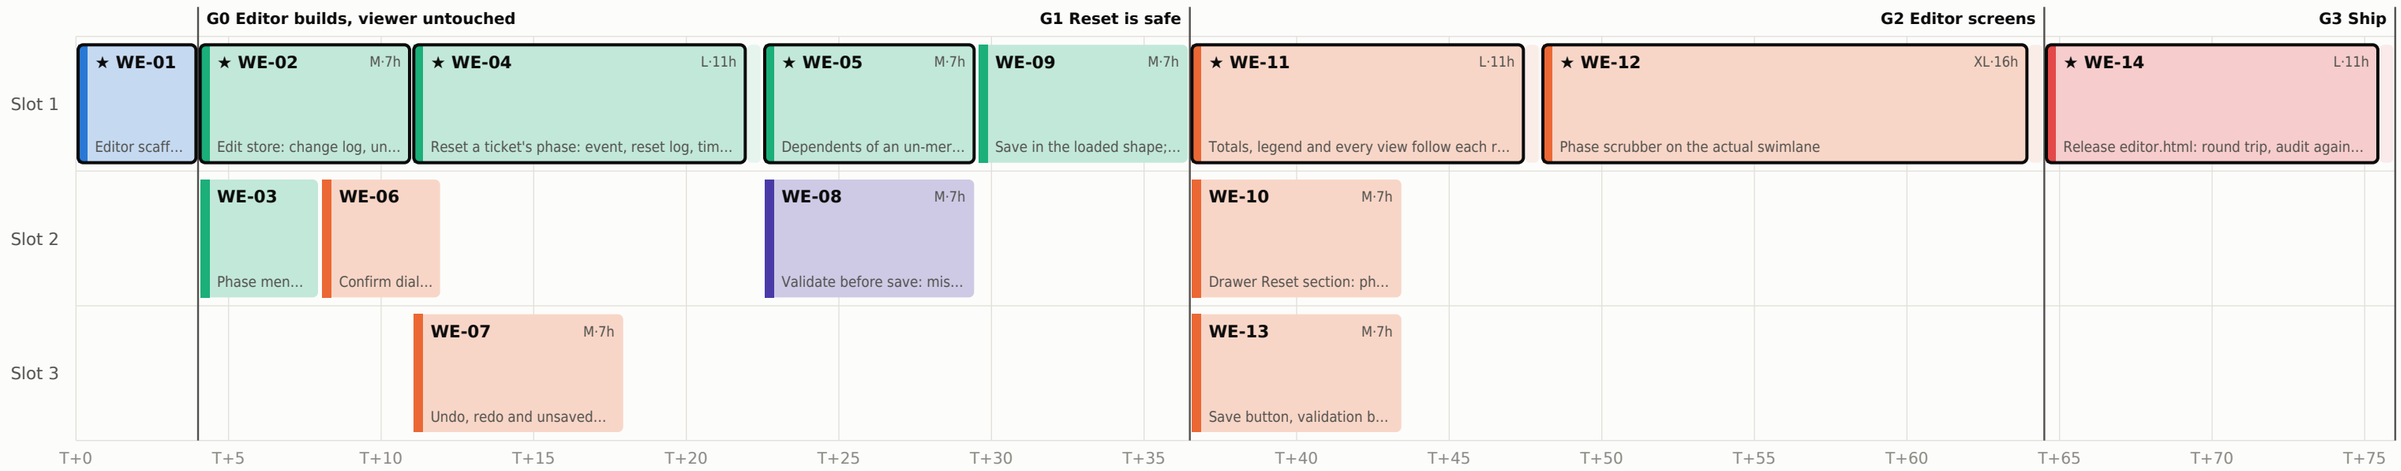

Estimate-hours on a continuous clock. Solid = the agent works; pale = an L/XL PR waits for approval before dependents start. A slot is reused the moment its agent finishes.

Step table — every merge moment

One row per moment something merges: what lands, the gate it reaches, what starts on which slot.

#	At	Merges	Gate	Starts (ticket → slot)	In flight
0	**T+0h**	start		★ WE-01 → 1	1
1	**T+4h**	★ WE-01	**G0 Editor builds, viewer untouched**	★ WE-02 → 1, WE-03 → 2	2
2	**T+8h**	WE-03		WE-06 → 2	2
3	**T+11h**	★ WE-02		★ WE-04 → 1, WE-07 → 3	3
4	**T+12h**	WE-06		—	2
5	**T+18h**	WE-07		—	1
6	**T+22h**	start		—	1
7	**T+22.5h**	★ WE-04		★ WE-05 → 1, WE-08 → 2	2
8	**T+29.5h**	★ WE-05, WE-08		WE-09 → 1	1
9	**T+36.5h**	WE-09	**G1 Reset is safe**	★ WE-11 → 1, WE-10 → 2, WE-13 → 3	3
10	**T+43.5h**	WE-10, WE-13		—	1
11	**T+47.5h**	start		—	1
12	**T+48h**	★ WE-11		★ WE-12 → 1	1
13	**T+64h**	start		—	1
14	**T+64.5h**	★ WE-12	**G2 Editor screens**	★ WE-14 → 1	1
15	**T+76h**	★ WE-14	**G3 Ship**	—	0

T+ = estimate-hours. Starts are ticket → slot. Detail per start: BUILD_PLAN.md.

Slot sequences

Start → merge in estimate-hours, per slot.

Slot	Tickets	Busy	Sequence
Slot 1	8	74h	★ WE-01 (0–4) → ★ WE-02 (4–11) → ★ WE-04 (11–22.5) → ★ WE-05 (22.5–29.5) → WE-09 (29.5–36.5) → ★ WE-11 (36.5–48) → ★ WE-12 (48–64.5) → ★ WE-14 (64.5–76)
Slot 2	4	22h	WE-03 (4–8) → WE-06 (8–12) → WE-08 (22.5–29.5) → WE-10 (36.5–43.5)
Slot 3	2	14h	WE-07 (11–18) → WE-13 (36.5–43.5)
